

Lab 2 (Problem Statement – 44)


Name : Samiksha B N

SRN: PES1UG24CS413


Section: 5G



Screenshots:

1)Jira backlog with Epics and User Stories and Story point assignments.

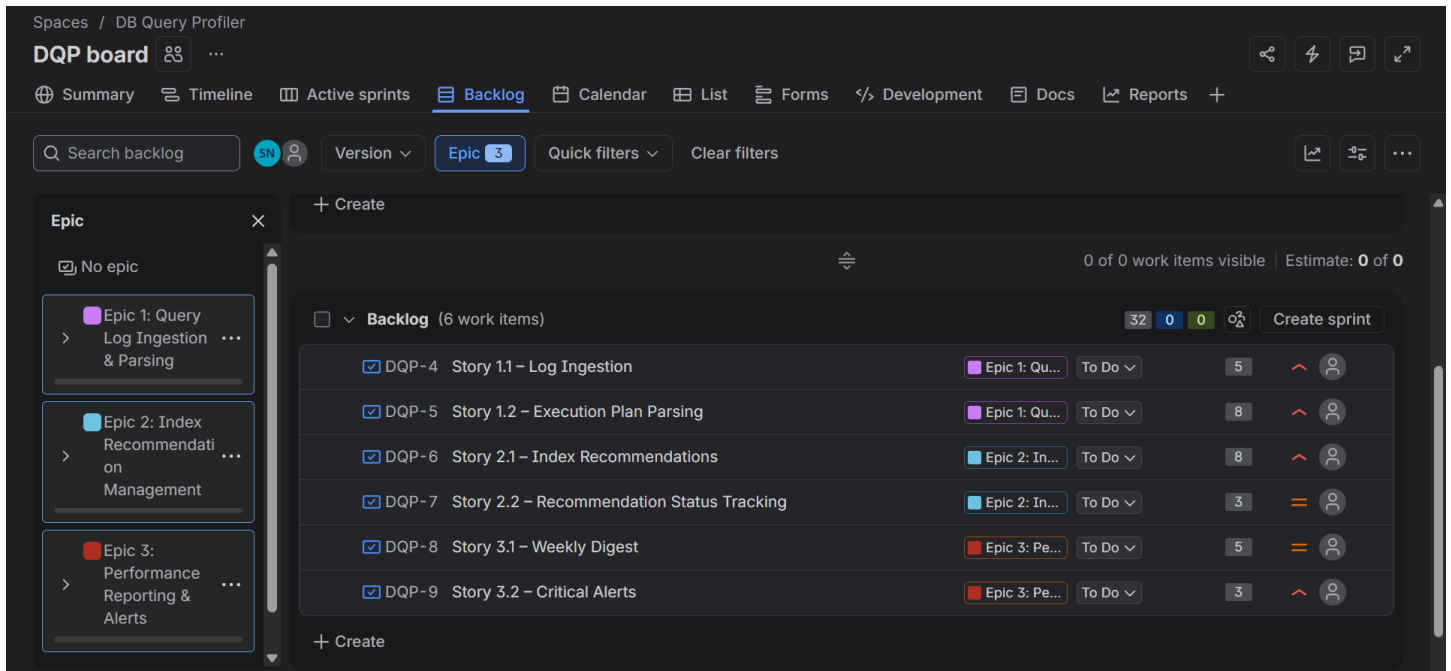

2)Sprint board for Sprint -1

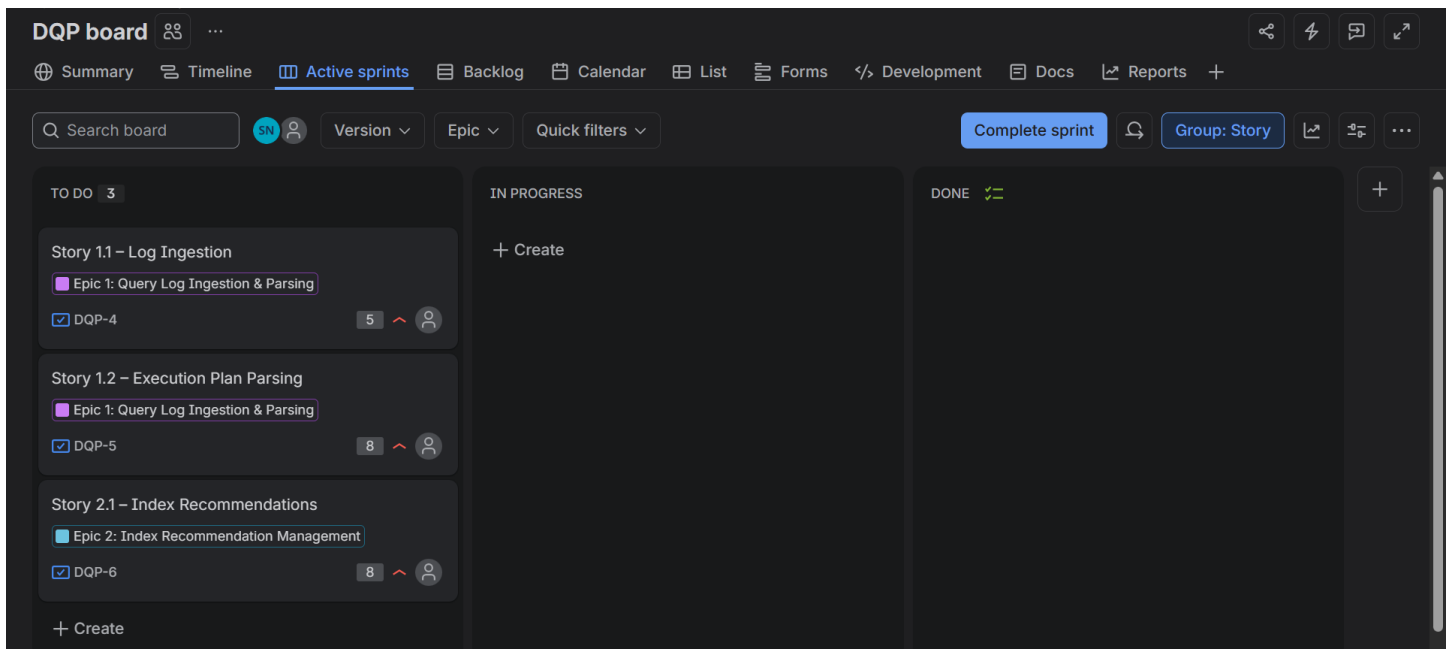

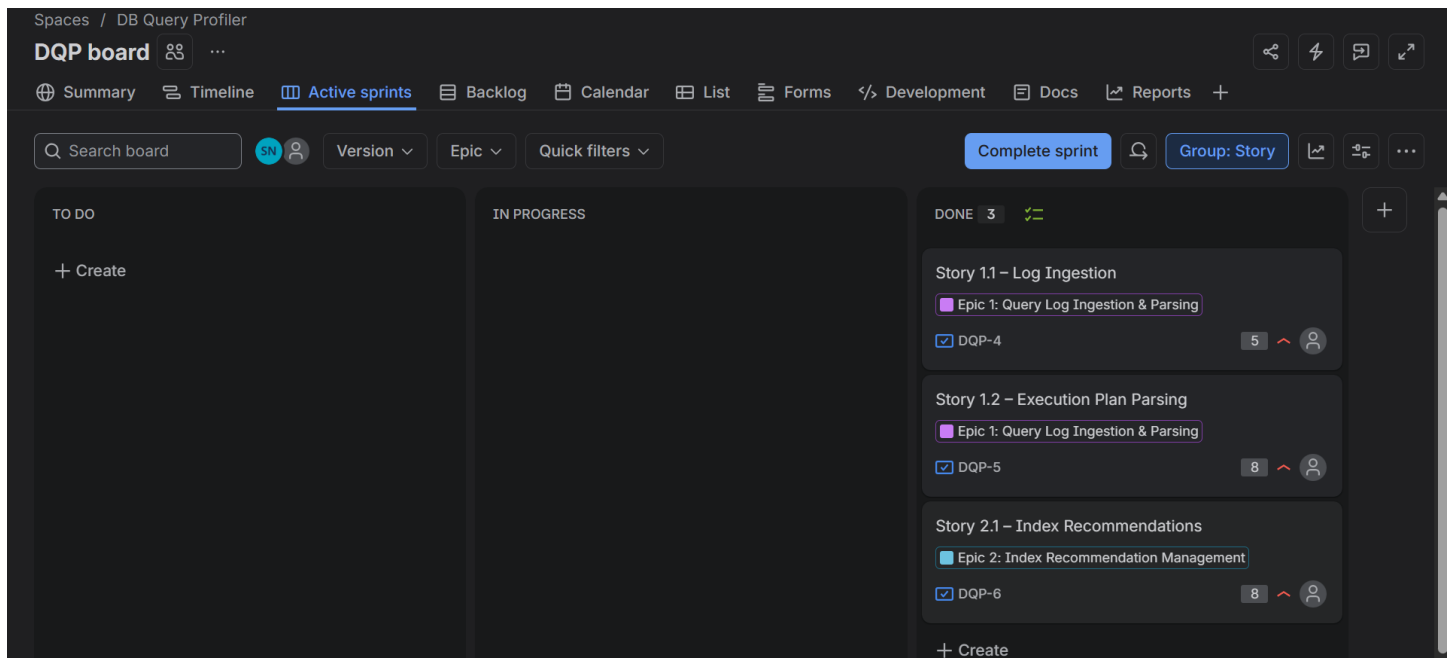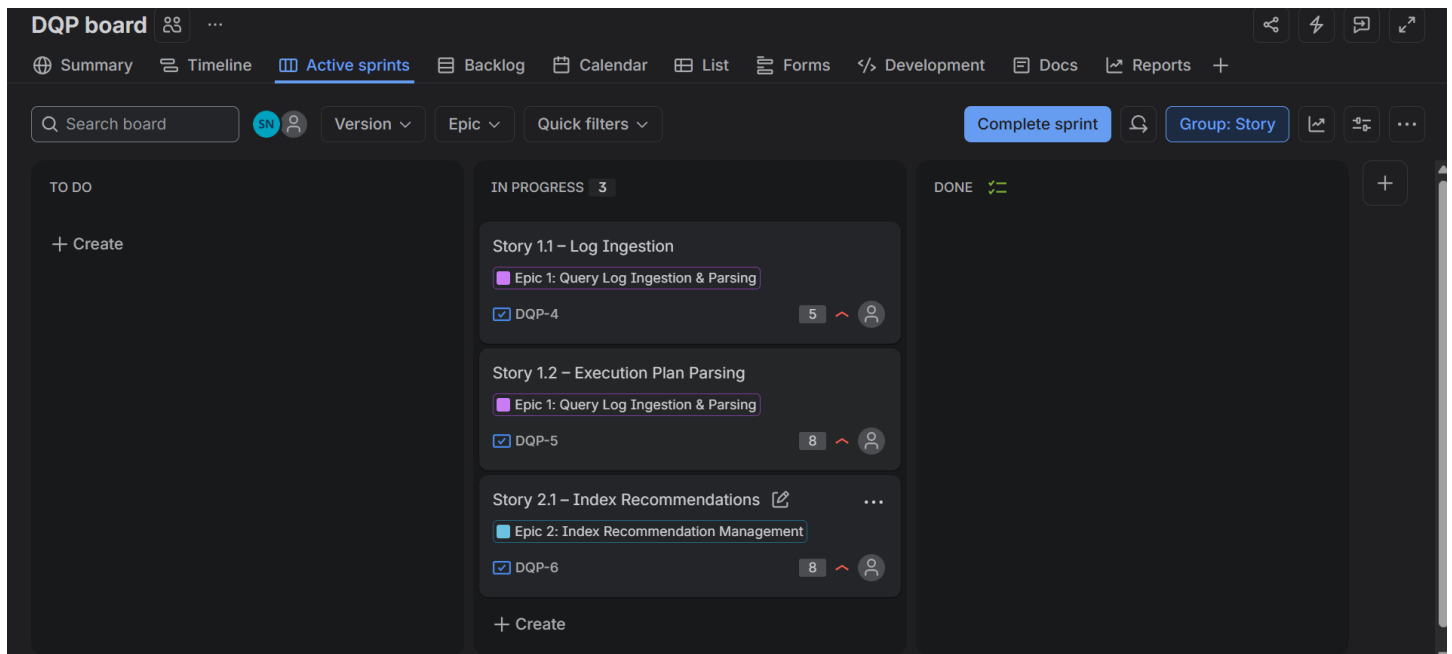

3) Sprint board for Sprint-2

DQP board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Reports

Search board

SN

Version

Epic

Quick filters

Complete sprint

Group: Story

TO DO 3

Story 2.2 – Recommendation Status Tracking

Epic 2: Index Recommendation Management

✓ DQP-7

3

=

Story 3.1 – Weekly Digest

Epic 3: Performance Reporting & Alerts

✓ DQP-8

5

=

Story 3.2 – Critical Alerts

Epic 3: Performance Reporting & Alerts

✓ DQP-9

3

<

+ Create

IN PROGRESS

+ Create

DONE

+ Create

Spaces / DB Query Profiler

DQP board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Reports

Search board

SN

Version

Epic

Quick filters

Complete sprint

Group: Story

TO DO

+ Create

IN PROGRESS 3

Story 2.2 – Recommendation Status Tracking

Epic 2: Index Recommendation Management

✓ DQP-7

3

=

Story 3.1 – Weekly Digest

Epic 3: Performance Reporting & Alerts

✓ DQP-8

5

=

Story 3.2 – Critical Alerts

Epic 3: Performance Reporting & Alerts

✓ DQP-9


3

<


+ Create

DONE

+ Create

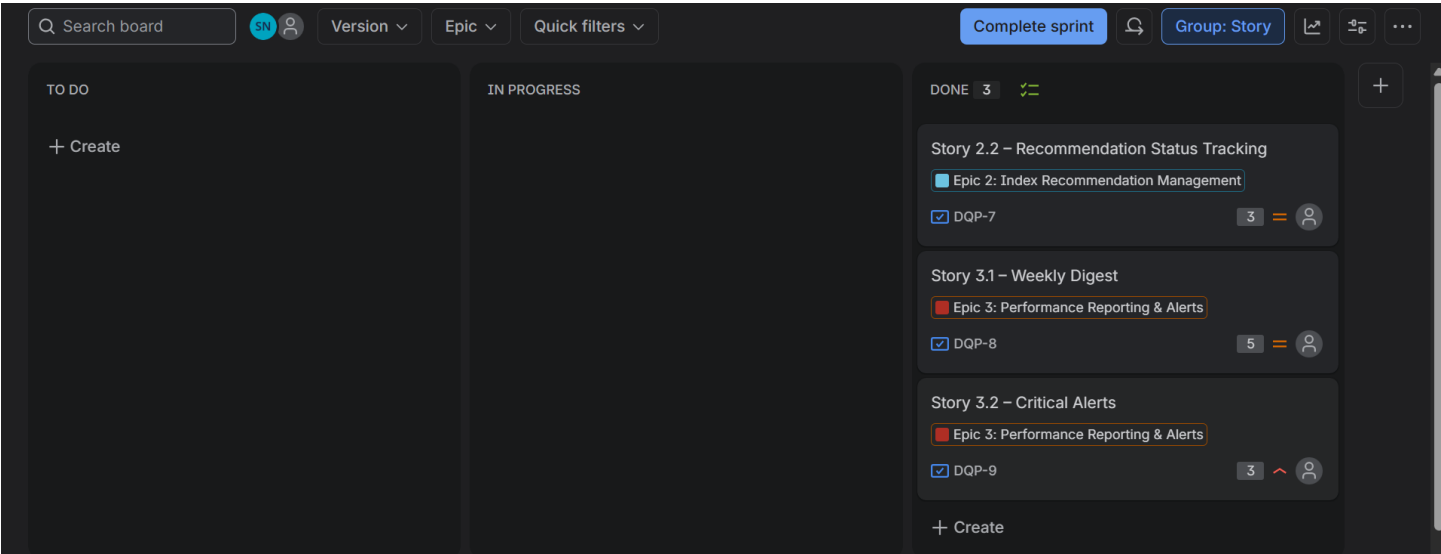

4) Burndown Chart for Sprint-1

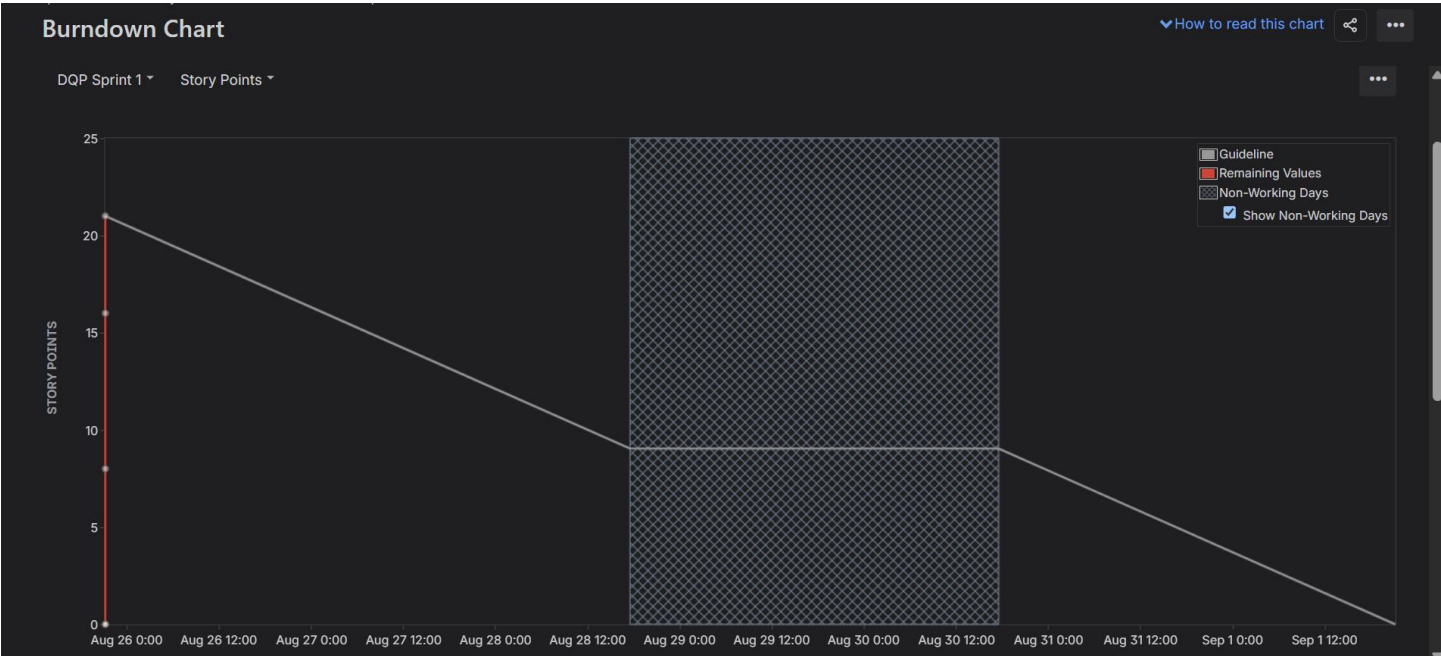

Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
25/Aug/26 9:09 PM	DQP-4	Sprint start		5		
	DQP-5			8		
	DQP-6			8		
	Total					21
25/Aug/26 9:10 PM	DQP-4	Burndown	Issue completed	5		16
	DQP-5	Burndown	Issue completed	8		8
	DQP-6	Burndown	Issue completed	8		0
	DQP-4	Sprint ended by Samiksha B N				0
	DQP-5					0
	DQP-6					0
	Total					0

5) Burndown Chart for Sprint-2



Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
25/Aug/26 9:11 PM	DQP-7	Sprint start		3		
	DQP-8			5		
	DQP-9			3		
	Total					11
	DQP-7	Burndown	Issue completed		3	8
	DQP-8	Burndown	Issue completed		5	3
	DQP-9	Burndown	Issue completed		3	0
	DQP-7	Sprint ended by Samiksha B N				0
	DQP-8					0
	DQP-9					0
	Total					0

Reflection Questions:

1. Did your estimations reflect the actual effort?

Broadly yes for the simpler, well-understood stories, Recommendation Status Tracking and Critical Alerts were estimated at 3 points each, and their scope (a status field and a threshold check) matched that estimate well. The two most complex stories, Execution Plan Parsing and Index Recommendations, were both estimated at 8 points because they involve interpreting arbitrary SQL execution plans across two different database engines. In a real sprint, this uncertainty likely means these two stories would need to be broken into smaller sub-tasks after the first planning-poker round revealed disagreement on scope.

2. Was your backlog well-prioritized?

Yes. The two High-priority foundational stories, Log Ingestion and Execution Plan Parsing were scheduled in Sprint 1 because every other Epic depends on ingested and parsed data being available first. Index Recommendations was also placed in Sprint 1 since it delivers the tool's core value proposition. The remaining Medium-priority stories (Recommendation Status Tracking, Weekly Digest) and the second High-priority story (Critical Alerts) were placed in Sprint 2, once the underlying data pipeline existed to support them.

3. How did your simulated sprint align with your plan?

Moving stories across To Do, In Progress and Done in Jira mirrored the intended dependency order: ingestion and parsing were completed first, which "unlocked" realistic completion of the recommendation-engine story. Sprint 1 carried more story points (21) than Sprint 2 (11), reflecting that foundational plumbing work is naturally heavier than the reporting features built on top of

it. All three Sprint 2 issues (DQP-7, DQP-8, DQP-9) were marked complete within minutes of starting the sprint, since this was a simulated sprint executed in a single sitting rather than a real week of development ,the *order* of completion matched the plan even though the *pace* was compressed.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart's red "remaining values" line dropped almost immediately from 11 to 0, falling well below the grey guideline for nearly the entire sprint duration instead of tracking a steady diagonal. In a real sprint, this pattern , finishing far ahead of the linear pace ,would be a signal that the team under-committed during sprint planning and could safely take on more work next sprint. Here, it's a direct result of the simulation being compressed into one session: all three issues ($3+5+3 = 11$ points) were completed back-to-back rather than spread across the week, so the chart shows an idealized "best case" rather than organic day-by-day progress.
